5018 N Derbigny
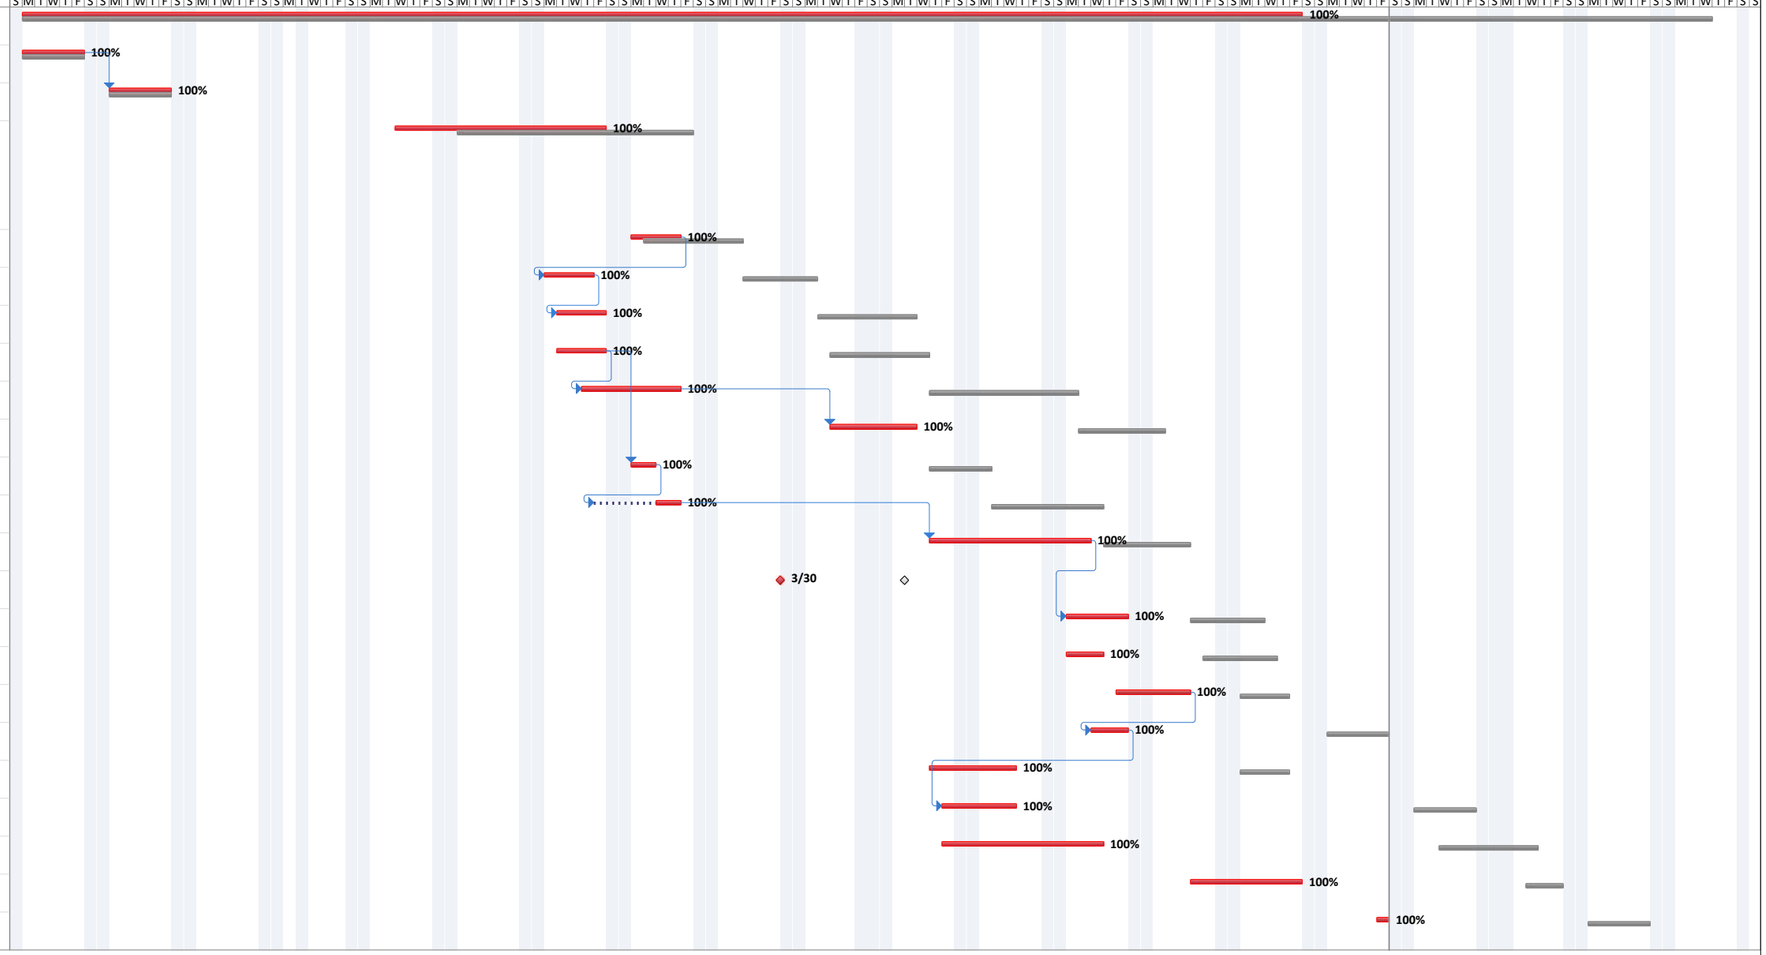
ID	Task Name	Actual Start	Actual Finish	Baseline Start	Baseline Finish
1	5018 N. Derbigny	Mon 1/30/12	Fri 5/11/12	Mon 1/30/12	Wed 6/13/12
2	Demo and Site Prep	Mon 1/30/12	Fri 2/3/12	Mon 1/30/12	Fri 2/3/12
3	Pilings and Underground Plumbing	Mon 2/6/12	Fri 2/10/12	Mon 2/6/12	Fri 2/10/12
4	Rough Framing Carpentry (including exterior doors, windows, porches & decks)	Wed 2/29/12	Fri 3/16/12	Mon 3/5/12	Fri 3/23/12
5	Roof Covering	Mon 3/19/12	Thu 3/22/12	Tue 3/20/12	Tue 3/27/12
6	Rough Electric	Mon 3/12/12	Thu 3/15/12	Wed 3/28/12	Mon 4/2/12
7	Rough Plumbing	Tue 3/13/12	Fri 3/16/12	Tue 4/3/12	Tue 4/10/12
8	Rough HVAC	Tue 3/13/12	Fri 3/16/12	Wed 4/4/12	Wed 4/11/12
9	Siding	Thu 3/15/12	Thu 3/22/12	Thu 4/12/12	Mon 4/23/12
10	Exterior Paint	Wed 4/4/12	Tue 4/10/12	Tue 4/24/12	Mon 4/30/12
11	Spray Foam Installation	Mon 3/19/12	Tue 3/20/12	Thu 4/12/12	Mon 4/16/12
12	Drywall	Fri 3/16/12	Thu 3/22/12	Tue 4/17/12	Wed 4/25/12
13	Interior Trim & Cabinets	Thu 4/12/12	Tue 4/24/12	Thu 4/26/12	Wed 5/2/12
14	HOS Notification	Fri 3/30/12	Fri 3/30/12	Mon 4/9/12	Mon 4/9/12
15	Final Electric	Mon 4/23/12	Fri 4/27/12	Thu 5/3/12	Tue 5/8/12
16	Final Plumbing	Mon 4/23/12	Wed 4/25/12	Fri 5/4/12	Wed 5/9/12
17	Final HVAC	Fri 4/27/12	Wed 5/2/12	Mon 5/7/12	Thu 5/10/12
18	Interior Paint	Wed 4/25/12	Fri 4/27/12	Mon 5/14/12	Fri 5/18/12
19	Solar	Thu 4/12/12	Wed 4/18/12	Mon 5/7/12	Thu 5/10/12
20	Floor Coverings	Fri 4/13/12	Wed 4/18/12	Mon 5/21/12	Fri 5/25/12
21	Pervious & Landscape	Fri 4/13/12	Wed 4/25/12	Wed 5/23/12	Wed 5/30/12
22	Punchout	Thu 5/3/12	Fri 5/11/12	Wed 5/30/12	Fri 6/1/12
23	CO Inspection	Fri 5/18/12	Fri 5/18/12	Mon 6/4/12	Fri 6/8/12
